Hillsborough Street Resurfacing Project

ASPHALT SURFACING, INC.

Project Start: Wed, 6/2/2021

Display Week: 1

TASK	ASSIGNED TO	PROGRESS	START	END
Mobilization & Milling				
Mobilization & SWPPP	ASI	0%	6/2/21	6/3/21
Striping Removals	Chrisp Co.	0%	6/4/21	6/5/21
Milling (Chateau Dr.)	ASI	0%	6/7/21	6/8/21
Milling (Hayne Rd.)	ASI	0%	6/14/21	6/15/21
Drain Inlet Replacement	ASI	0%	7/5/21	7/5/21
AC Paving				
Base Repair and Grind	ASI		6/23/21	6/25/21
Overlay (Chateau Dr.)	ASI		6/24/21	6/24/21
Overlay (Hayne Rd.)	ASI		6/24/21	6/24/21
Surface Treatments				
Spray Herbicide	ASI	0%	6/23/21	6/24/21
Crackfill	ASI	0%	7/5/21	7/9/21
Microsurfacing	ASI	0%	7/13/21	7/14/21
Striping / Bike Signs	ASI	0%	7/19/21	7/21/21
Adjust Utiles to grade During Paving			6/10/21	6/29/21
Insert new rows ABOVE this one				

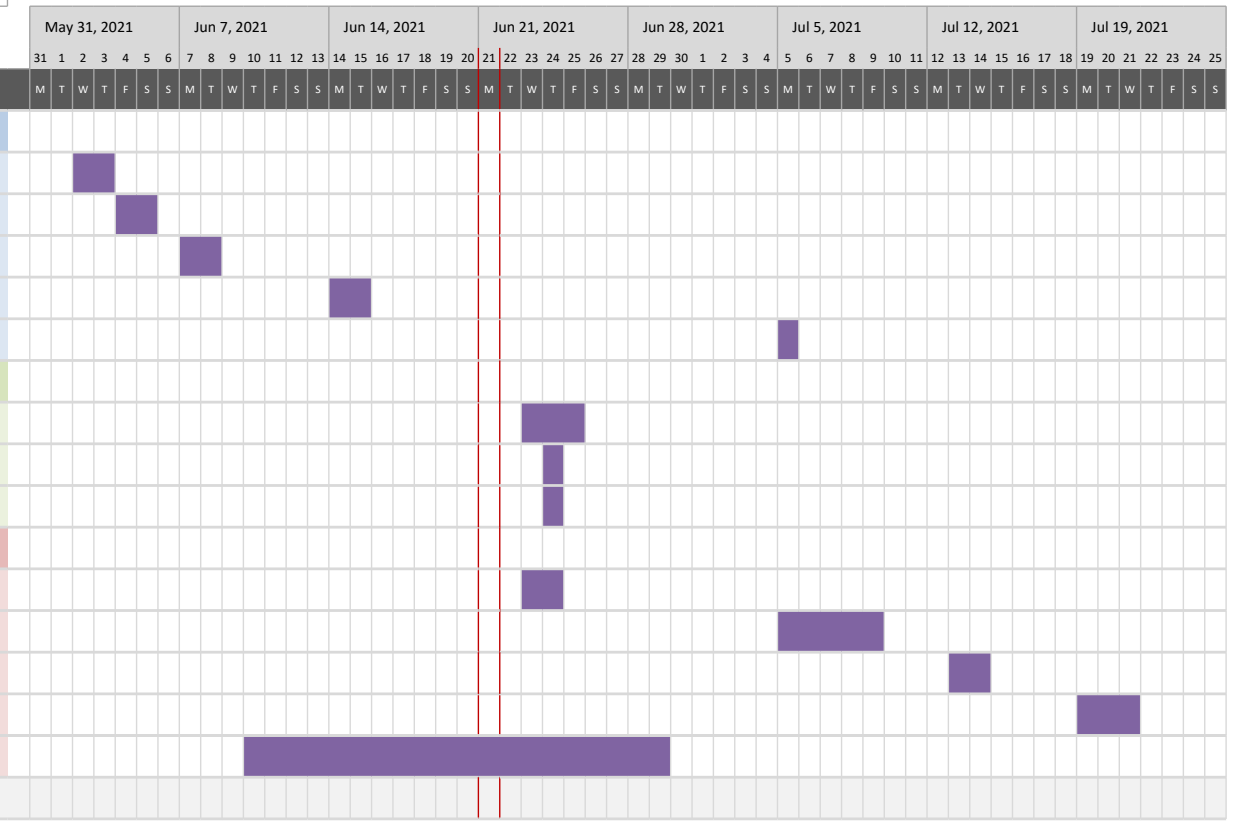

Notes:

1. Areas that receive grinding shall be resurfaced within (7) calendar days from the time that the planing cuts are made.
2. An approved herbicide shall be sprayed in all cracks at least (10) calendar days prior to the application of sealant.
3. All crack seal shall be done within a minimum 72 hours prior to microsurfacing treatment.
4. Each street shall receive permanent stop limit lines and crosswalks no sooner than (7) days or no later than 10 days following resurfacing of the street.
